

# PROJECT PROGRESS UPDATE

CITIZENS' OVERSIGHT COMMITTEE MEETING,  
SEPTEMBER 13, 2021

## TOPICS TO BE COVERED

- Pacific Sky School
- Del Mar Heights School Rebuild
- Del Mar Hills Academy Modernization
- Districtwide Projects



# PACIFIC SKY SCHOOL CONSTRUCTION

# PACIFIC SKY SCHOOL

- Time-lapse Video
- May 17, 2021 – August 16, 2021



# PACIFIC SKY SCHOOL

- Construction Ongoing
- Anticipated Student Start – August 15, 2022
- Anticipated Full Site Completion – January 2023



# DEL MAR HEIGHTS SCHOOL REBUILD



# DEL MAR HEIGHTS SCHOOL REBUILD

- CEQA – Focused EIR
  - Board Approved – June 30, 2021
- Litigation
  - Court Order determining that the District had fully complied with CEQA – July 19, 2021
  - Appeal filed August 6, 2021
- Coastal Development Permit
  - Resubmitted
- Construction
  - Upon receipt of the Coastal Development Permit



# DEL MAR HILLS ACADEMY MODERNIZATION





# DEL MAR HILLS ACADEMY MODERNIZATION

- Community Planning Sessions
  - June 3, 2021
  - September 20, 2021
  - October 2021
- Board Review October 27, 2021



# DEL MAR HILLS ACADEMY MODERNIZATION

- Review input from staff and community
- Structural Review
- Original and modernization plan review
- Develop design option(s)
- Analyze options related to budget
- Prepare for September community engagement session



# DISTRICTWIDE PROJECTS



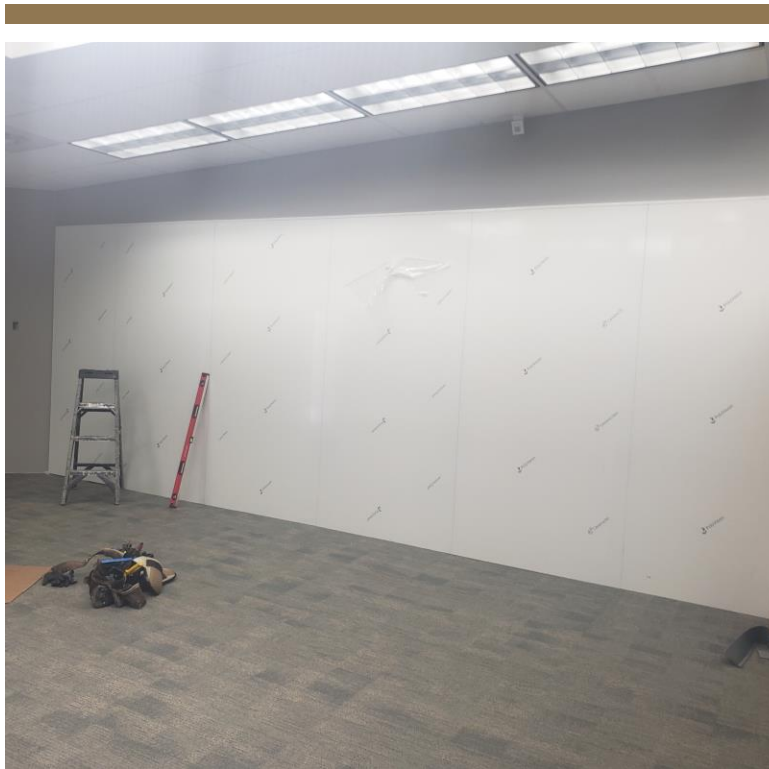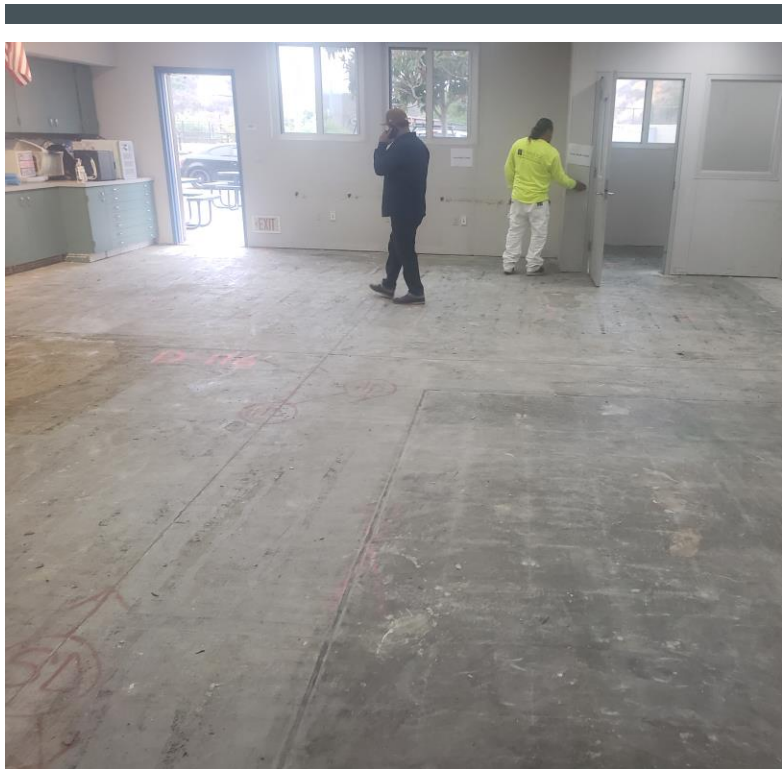


# MODERNIZED LEARNING ENVIRONMENTS





# MODERNIZED LEARNING ENVIRONMENTS

- K-6
- STEAM+
- Library / Innovation Center

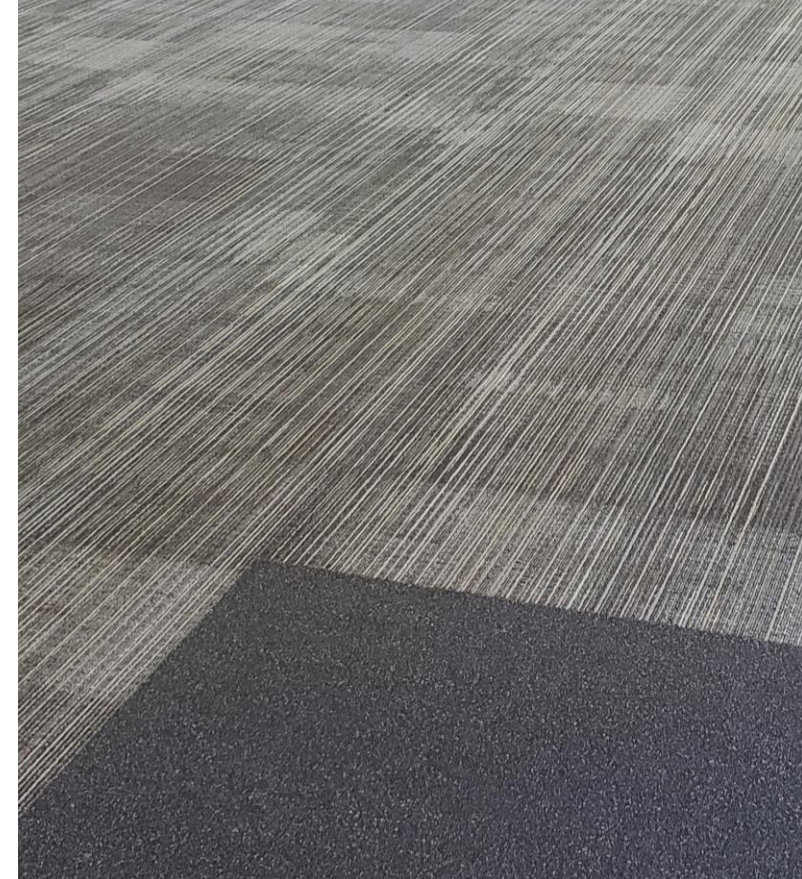





# SYCAMORE RIDGE PLAY STRUCTURE



# QUESTIONS
