PROJECT PROGRESS UPDATE

CITIZENS' OVERSIGHT COMMITTEE MEETING, DECEMBER 7, 2020

TOPICS TO BE COVERED

- Capital Improvement Plan Review
- Pacific Highlands Ranch School #9
- Del Mar Heights School Rebuild
- Del Mar Hills Academy Modernization

CAPITAL IMPROVEMENT PLAN REVIEW

- Consolidation of projects
- Review of delay impacts
- Board Update January/February
- COC Update February/March

PACIFIC
HIGHLANDS
RANCH
SCHOOL #9



PACIFIC HIGHLANDS RANCH SCHOOL #9




- Design symposium process Complete
- Community Input Complete
- CEQA Complete
- Land Purchase Complete
- Coastal Development Permit Submitted
- DSA
 - Increment I approved
 - Increment 2 submittal September 22, anticipated approval early 202 l
- Construction Winter 2021- Spring/Summer 2022*

DEL MAR HEIGHTS SCHOOL REBUILD



DEL MAR HEIGHTS SCHOOL REBUILD

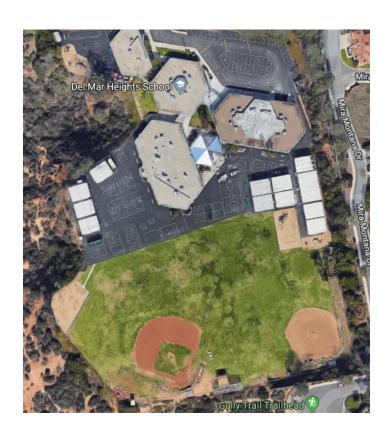

* Dates are estimates

- Design symposium process Complete
- Community Input Complete
- CEQA Complete
 - Litigation hearing November 18, 2020
 - Result -
- Coastal Development Permit Submitted
- DSA
 - Increment I approved
 - Increment 2 approved
- Construction TBD (pending Coastal Development Permit)*

DEL MAR HILLS ACADEMY MODERNIZATION

DEL MAR HILLS ACADEMY MODERNIZATION



- Design symposium process TBD
- Community Input —TBD
- CEQA TBD
- DSA TBD
- Construction TBD

QUESTIONS
